

PEGATRON

Navigate the future >

BG6
PVN

2025 PVN FME Q1 Work Report

Dept.: BG6-Manufacturing&Operation Management Center.-Vietnam
Manufacturing Div.-PVN1 Factory-FME Dept.-Automation Sec.

Name: Leon Than 申玉龍

Date: 2025/03/20



Self-Work Responsibilities

1. Learning AI SOP equipment and practice setup AI SOP production line in factory.

- Adjust camera, setup layout.
- Test computer.
- Inference server.
- AI SOP working process.
- Setup programming, get images and training model.
- Push data to the inference server.
- Run program in line and check model result.
- Note the programming error and find the way to fix.

2. Learning AOI equipment and practice setup AOI production line in factory.

- Setup position camera to check all part of devices.
- Adjust camera, setup layout.
- Test computer.
- Inference server.
- AOI working process.
- Learn and practice how to adjust camera and setup layout by Pylon Viewer.
- Learn and practice how to get images, cut background and training points of AOI equipments

Self-Work Responsibilities

3. Assemble and install AOI equipment in line 4A CISCO EZ1K/Lightsaber 48P and 4C Somerset-Infra.

- Assemble EZ1K/Lightsaber 48P Outernal Inspection AOI and EPSON RC+ equipment.
- Assemble Infra Outernal Inspection AOI and motor equipment.
- Motor program setting, coordinate adjustment.
- Robot program setting, coordinate adjustment.
- Improve coordinate recognition and vision training.
- Improve the program, create connection between vision and robot.
- Test program with sample.
- Note the programming error and find the way to fix.

4. Install the AOI python program outernal inspection in line 4C CISCO Somerset-Infra, 4J SKY, 4K Panasonic project.

- Installing machines and programs.
- Tweaking and improving Python code.
- Tweaking and debugging cameras.
- Model image processing.
- Model training and testing.
- Error handling and system improvement.

5. Deploy the program and run online on the system

- Install necessary libraries, frameworks and tools.
- Verify connections with server.
- Testing and monitoring.
- Run online and maintain the System.

Self-Work Responsibilities

6. Staffing and personnel management

- Organize and Schedule work for members in AOI Team.
- Training and Development of new members.
- Creating a Positive Work Environment.
- Write weekly and monthly statistical reports.
- Respond to AOI progress with QA and management.
- Send email notifications to IE, ME, and QA when the AOI station test is online.
- Contact related departments when handling work

Q1-2025 Work Results

Time	Work Results
2024 Q4	Complete the line 4A (CISCO EZ1K/Lightsaber 48P) internal inspection program system and operate online.
	Complete the line 4B (CISCO EZ1K/Lightsaber 8P) internal inspection program system and operate online.
	Complete the line 4C (CISCO WP-Infra) outernal inspection program system and operate online.
	Complete model training the line 4A, 4B(CISCO EZ1K/Lightsaber 48P/8P) outernal inspection program system.
2025 Q1	Complete the line 4J (CISCO SKY) outernal inspection program system and operate online.
	Complete the line 4B (CISCO EZ1K/Lightsaber 8P) outernal inspection program system and operate online.
	Complete the line 4B (CISCO EZ1K/Lightsaber 8P) label check program system and waiting operate online.
	Complete model training the line 4C (CISCO WP-Somerset) outernal inspection program system.

Detailed Description of Work Results

CISCO EZ1K/Lightsaber 8P Internal inspection

Component: AOI C1300_8T_E_2G v3.2.19

Test Mode Setting Mode On_line OP ID: V24001655 Device ID: 315366

Since: 2025-03-17 13:19:56
Pass: 132 Fail: 0 Size err: 0

11ISN OK!!(L)(SM)-DATA:[2567120200611] PASSI-(TSP_SSD_INPUTDATA)00

Test Status


PASS

Information

Brightness avg: 76
Camera Status: Ready
- Exp Time (ms): 15.015
Barcode Status: Ready
RFID R/W Status: N/A
PLC Status: led green on: Failed

Input ISN
2567120200095

Screw
Capacitor
Heatsick
Battery

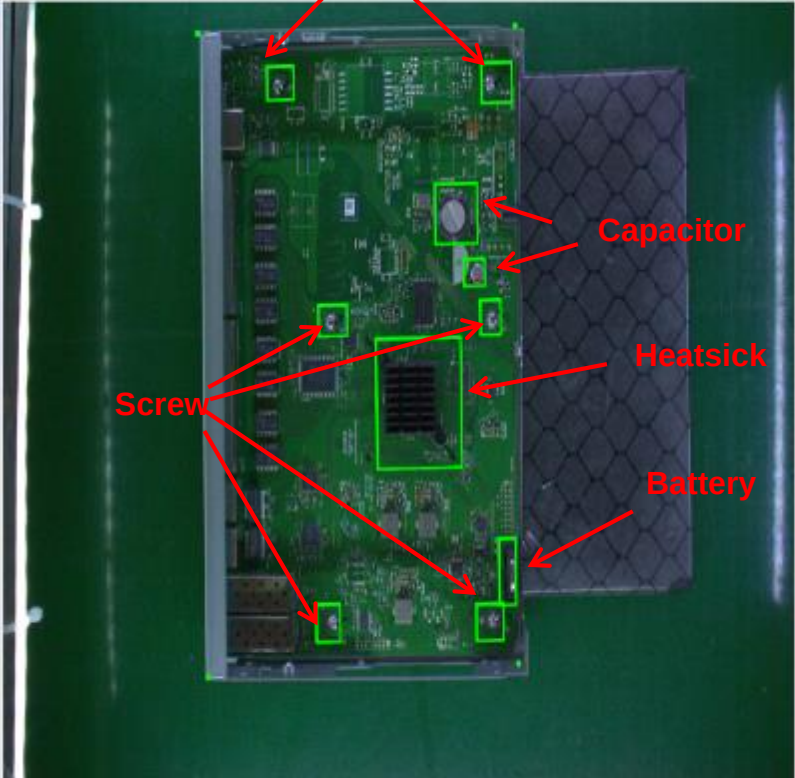

MO_ROUTE

SEQ	SHOP	LINE	GRPNM	STEPNM	OP	OPNM	MO	STATUS
1	V	V54NW02	ASSY INPUT	投板	V24001719	LƯƠNG MẠNH KIỂM	25678472	無錯誤
2	V	V54NW02	WRITE MAC	Pre-test	V24001315	PHẠM NGỌC HUYNH	25678472	無錯誤
3	V	V54NW02	ASSY KP INPUT4	CHECK 下蓋	V23003520	LÊ VĂN TUẤN	25678472	無錯誤
4	V	V54NW02	ASSY KP INPUT1	Link電源	V24001656	VŨ THỊ HỒNG NHUNG	25678472	無錯誤
5	V	V54NW02	ENCLOSURE INSPECTION	INTERNAL INSPECTION	V24001655	HÀ VĂN LONG	25678472	無錯誤
6	V	V54NW02	ASSY KP INPUT3	列印機台Label	S09155978	陳超	25678472	無錯誤
7	V	V54NW02	ASSY KP INPUT2	CHECK 上蓋	V24002129	PHẠM THỊ LAN ANH	25678472	無錯誤
8	V	V54NW02	ASSY KP INPUT5	CHECK ML	V24003972	ĐÀO THỊ HUỆ	25678472	無錯誤
9	V	V54NW02	ASSY IN-CHECK	組裝外觀總檢	V24003255	LƯƠNG THÀNH LONG	25678472	無錯誤
10	V	V54NW02	AGING INPUT	Burn-In Input	V24002129	PHẠM THỊ LAN ANH	25678472	無錯誤
11	V	V54NW01	TEST AGING	Burn-In output	V24004556	TRẦN ĐỨC TÙNG	25678472	無錯誤
12	V	V54NW02	FINALTEST1	Final test	V24001095	TẠ THÀNH TRƯỜNG	25678472	重測

1

STATION	GRP	INPUT	RW INPUT	Total Input	First Defect	First Yield Rate
Pre-test	TW4	0	1	1	0	100.00%
CHECK 下蓋	A14	509	1	510	0	100.00%
Link電源	A11	508	1	509	0	100.00%
INTERNAL INSPECTION	AD4	508	1	509	3	99.41%
列印機台Label	A13	508	3	511	0	100.00%
CHECK 上蓋	A12	508	3	511	0	100.00%
CHECK ML	A15	507	2	509	0	100.00%
組裝外觀總檢	AD0	507	1	508	0	100.00%
Burn-In Input	AG1	506	3	509	0	100.00%
Burn-In output	TA0	509	3	512	80	84.38%
Final test	TS3	550	2	552	18	96.74%
Final check	TFC	551	1	552	3	99.46%
Software Download	TS0	551	2	553	3	99.46%
AOI check	KV0	562	0	562	0	100.00%
FQC	Q01	557	0	557	0	100.00%
	K07	536	0	536	0	100.00%
	T05	536	24	560	0	100.00%
Check Acc	PAK1	537	24	561	0	100.00%
OQC	OQC2	33	0	33	10	69.70%
	WEC	513	25	538	0	100.00%
	K10	512	128	640	0	100.00%
	WET	512	128	640	0	100.00%
	K02	528	168	696	0	100.00%
	W90	954	78	1032	0	100.00%
Total:		12002	599	12601	117	97.88%

1

Detailed Description of Work Results

CISCO EZ1K/Lightsaber 48P Internal inspection

Component_A0 C1300-48P-4G v3.2.13

Test Mode Setting Mode On_line OP ID: V24004004 Device ID: 314462

Since: 2025-03-17 09:33:29
Pass: 176 Fail: 16 Size err: 0


Test Status

PASS

Information

Brightness avg: 91
Camera Status: Ready
- Exp Time (ms): 9.997
Barcode Status: Ready
RFID RAW Status: N/A
PLC Status: led green on: Failed

Input ISN: 2567384700662

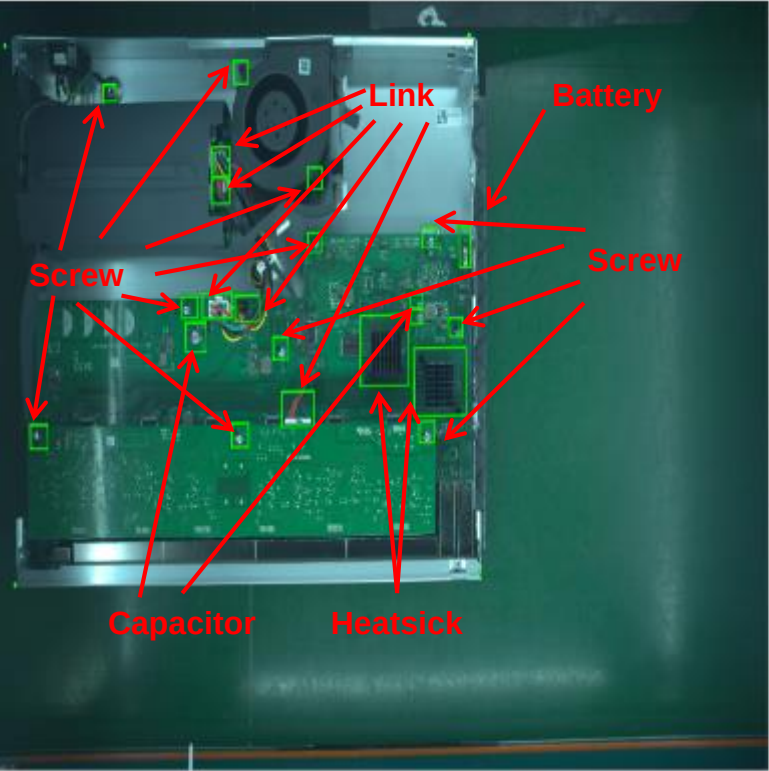

MO_ROUTE							
SEQ	SHOP	LINE	GRPNM	STEPM	OP	OPNM	MO STATUS
1	V	V54NW01	ASSY INPUT	投板	V24001719	LƯƠNG MẠNH KIỂM	25648069 無錯誤
2	V	V54NW01	WRITE MAC	Pre-test	V24001315	PHẠM NGỌC HUYNH	25648069 無錯誤
3	V	V54NW01	ASSY KP INPUT4	CHECK 下蓋	V25002496	NGUYỄN VĂN QUỐC	25648069 無錯誤
4	V	V54NW01	ASSY KP INPUT1	Link電源	V24005622	TRẦN NGUYỄN TRUNG	25648069 無錯誤
5	V	V54NW01	ENCLOSURE INSPECTION	INTERNAL INSPECTION	V23005542	LƯU MAI ANH	25648069 無錯誤
6	V	V54NW01	ASSY KP INPUT3	列印機台Label	S18051818	葉敬堃	25648069 無錯誤
7	V	V54NW01	ASSY KP INPUT2	CHECK 上蓋	V25002482	NGUYỄN THỊ HOA	25648069 無錯誤
8	V	V54NW01	ASSY KP INPUT5	CHECK ML	V25002452	LÔ THỊ TRANG	25648069 無錯誤
9	V	V54NW01	ASSY IN-CHECK	組裝外觀總檢	V25002483	LÔ THỊ ĐỨC	25648069 無錯誤
10	V	V54NW01	AGING INPUT	Burn-In Input	V24004458	NGUYỄN VĂN TỐI	25648069 無錯誤
11	V	V54NW01	TEST AGING	Burn-In output	V24004458	NGUYỄN VĂN TỐI	25648069 無錯誤
12	V	V54NW01	TEST CURRENT TEST	Burn-In output check	V24001999	NGUYỄN VĂN HUYỀN	25648069 無錯誤
13	V	V54NW01	HI-PORT SEC TEST	Hi-pot test	V24001999	NGUYỄN VĂN HUYỀN	25648069 無錯誤
14	V	V54NW01	FINALTEST1	Final test	V24004428	NGUYỄN QUANG KHẢI	25648069 無錯誤

1						
STATION	GRP	INPUT	RW INPUT	Total Input	First Defect	First Yield Rate
投板	A10	473	0	473	0	100.00%
Pre-test	TW4	466	2	468	92	80.34%
CHECK 下蓋	A14	425	13	438	0	100.00%
Link電源	A11	425	13	438	0	100.00%
INTERNAL INSPECTION	AD4	427	13	440	11	97.50%
列印機台Label	A13	426	19	445	0	100.00%
CHECK 上蓋	A12	426	19	445	0	100.00%
CHECK ML	A15	425	15	440	0	100.00%
組裝外觀總檢	AD0	423	13	436	2	99.54%
Burn-In Input	AGI	421	21	442	0	100.00%
Burn-In output	TA0	267	15	282	81	71.28%
Burn-In output check	TG0	275	11	286	0	100.00%
Hi-pot test	TH0	294	11	305	0	100.00%
Final test	TS3	295	10	305	18	94.10%
Final check	TFC	301	3	304	2	99.34%
code upgrade	T7A	31	0	31	1	96.77%
Software Download	TS0	297	31	328	5	98.48%
包裝外觀總檢	AP01	314	5	319	1	99.69%
FQC	Q01	334	0	334	3	99.10%
	K07	335	0	335	0	100.00%
	T05	335	0	335	0	100.00%
Check Acc	PAK1	333	3	336	0	100.00%
OQC	OQC2	29	0	29	2	93.10%
	WEC	335	0	335	0	100.00%
	K10	329	0	329	0	100.00%
	WET	327	0	327	0	100.00%
	K02	360	0	360	0	100.00%
	W90	862	2	864	0	100.00%
Total:		9990	219	10209	218	97.47%

Detailed Description of Work Results

CISCO Somerset-Infra outernal AOI

Appearance Inspection Model AOI (Vire) Model Version: V04.02.20241130121842 864650 Edge Test Version: 1.0.0.1

Loaded 运行模式(Run) 运行速度(Run) 停止(Stop) 返回待机后停止(Stop after clear) 重新测试前重置(Result)

站位名称	SN
3KA01	PVN291219K4

Pass Fail

112 32

投入总数 良率

144 77.78

Screw Label

Net

PASS

Pass---AOI上传失败

测试 Setting I/O Interface 故障设置

当前运行设备: infor_3

MO_ROUTE								
SEQ	SHOP	LINE	GRPNM	STEPNM	OP	OPNM	MO	STATUS
1	V	60VN3S01	SMT INPUT	INPUT-1	V23002288	ĐỖ THỊ THÙY	25657261	無錯誤
2	V	60VN3S04	SMT AOI1	爐後AOI-1	V25001768	NGUYỄN LÊ QUYỀN	25657261	重測
3	V	60VN3S04	SMT AOI1 REPAIR		V25001768	NGUYỄN LÊ QUYỀN	25657261	無錯誤
4	V	60VN3S04	SMT AOI1	爐後AOI-1	V25001768	NGUYỄN LÊ QUYỀN	25657261	無錯誤
5	V	60VN3S01	SMT AOI2	爐後AOI-2	V24004975	ĐÌNH ĐỨC QUANG	25657261	重測
6	V	60VN3S01	SMT AOI2 REPAIR		V24004975	ĐÌNH ĐỨC QUANG	25657261	無錯誤
7	V	60VN3S01	SMT AOI2	爐後AOI-2	V24004975	ĐÌNH ĐỨC QUANG	25657261	無錯誤
8	V	60VN3S01	SMT DOWN VISUAL	爐後VI-2	V24000349	ĐỖ NGỌC ÁNH	25657261	無錯誤
9	V	VNDIPS01	DIP INPUT		V24000942	LỘC THỊ TIẾN	25657265	無錯誤
10	V	VNDIPS01	DIP 後目檢		V24000942	LỘC THỊ TIẾN	25657265	無錯誤
11	V	V54NW03A	ASSY INPUT	投板	V24001719	LƯƠNG MANH KIỂM	25649094	無錯誤
12	V	V54NW03A	PRE VISUAL	PRETEST	V24002020	VŨ VIỆT VÂN	25649094	無錯誤
13	V	V54NW03A	UPSTREAM-CAL1	Wireless test	V24005868	TRƯƠNG VIỆT HOÀNG	25649094	無錯誤
14	V	V54NW03B	ASSY KP INPUT3	Assy Input3	S18051818	葉敬瑩	25649094	無錯誤
15	V	V54NW03A	TEST CALIBRATION	Antenna Verification	V24002020	VŨ VIỆT VÂN	25649094	無錯誤
16	V	V54NW03A	TEST WIRELESS	Firmware Download	V24005868	TRƯƠNG VIỆT HOÀNG	25649094	無錯誤
17	V	V54NW03A	SPECTRUM ANALYZER TEST	ACT2	V24002020	VŨ VIỆT VÂN	25649094	無錯誤
18	V	V54NW03A	PACKING1	AP01	V24002407	THAN NGOC LONG	25649094	無錯誤
19	V	V54NW03A	OQC packing前離線驗		V25002132	VU VAN VINH	25649094	無錯誤
20	V	V54NW03	PACKING	PACKING	S18051818	葉敬瑩	25649094	無錯誤
21	V	V54NW03A	WEITHT	WEITHT	S18051818	葉敬瑩	25649094	無錯誤
22	V	V54NW03	PACKING BOXing		S18051818	葉敬瑩	25649094	無錯誤
23	V	V54NW03	PACKING WEIGHT		S18051818	葉敬瑩	25649094	無錯誤
24	V	VF15F01A	WE 90		S09605560	信帥	25649094	無錯誤

1	STATION	GRP	INPUT	RW INPUT	Total Input	First Defect	First Yield Rate
	投板	AI0	417	0	417	0	100.00%
		AI1	1	0	1	0	100.00%
	PRETEST	T70	412	2	414	45	89.13%
	Wireless test	TY4	369	1	370	3	99.19%
	Assy Input3	AI3	404	13	417	0	100.00%
	Antenna Verification	TA6	390	13	403	12	97.02%
	Firmware Download	TW2	397	0	397	3	99.24%
	ACT2	TAS	392	0	392	4	98.98%
	AP01	AP01	466	0	466	2	99.57%
		Q01	463	0	463	0	100.00%
	PACKING	K10	477	0	477	0	100.00%
	WEITHT	WET	472	0	472	0	100.00%
		K01	472	0	472	0	100.00%
		K02	512	0	512	0	100.00%
		W90	512	0	512	0	100.00%
	Total:		6156	29	6185	69	98.88%
1							

Detailed Description of Work Results

CISCO EZ1K/Lightsaber 8P Eternal AOI Inspection




MO_ROUTE							
SEQ	SHOP	LINE	GRPNM	STEPNM	OP	OPNM	MO STATUS
1	V	V54NW02	ASSY INPUT	投板	V24001719	LƯƠNG MẠNH KIỂM	25678475 無錯誤
2	V	V54NW02	WRITE MAC	Pre-test	V24001315	PHẠM NGỌC HUYNH	25678475 無錯誤
3	V	V54NW02	ASSY KP INPUT4	CHECK 下蓋	V23003520	LÊ VĂN TUÂN	25678475 無錯誤
4	V	V54NW02	ASSY KP INPUT1	Link電源	V24001656	VŨ THỊ HỒNG NHUNG	25678475 無錯誤
5	V	V54NW02	ENCLOSURE INSPECTION	INTERNAL INSPECTION	V24001655	HÀ VÂN LONG	25678475 無錯誤
6	V	V54NW02	ASSY KP INPUT3	列印機台Label	S18051818	黨敬瑩	25678475 無錯誤
7	V	V54NW02	ASSY KP INPUT2	CHECK 上蓋	V24002129	PHẠM THỊ LAN ANH	25678475 無錯誤
8	V	V54NW02	ASSY KP INPUT5	CHECK ML	V23001614	NGUYỄN PHƯƠNG HOA	25678475 無錯誤
9	V	V54NW02	ASSY IN-CHECK	組裝外觀總檢	V24003255	LƯƠNG THÀNH LONG	25678475 無錯誤
10	V	V54NW02	AGING INPUT	Burn-In Input	V24002129	PHẠM THỊ LAN ANH	25678475 無錯誤
11	V	V54NW01	TEST AGING	Burn-In output	V24002210	BÙI QUANG THIÊN	25678475 無錯誤
12	V	V54NW02	FINALTEST1	Final test	V24006345	DƯƠNG THẾ VINH	25678475 無錯誤
13	V	V54NW02	TEST FINAL CHECK	Final check	V24001095	TA THÀNH TRƯỜNG	25678475 無錯誤
14	V	V54NW02	11-SN & ADDR. CHECK	Software Download	V23001431	NGUYỄN VĂN NAM	25678475 無錯誤
15	V	V54NW02	PACK POST VISUAL	AOI check	V24002407	THAN NGOC LONG	25678475 無錯誤
16	V	V54NW02	OQC packing前離線驗	FQC	V24003535	PHAM THI HOAI THU	25678475 無錯誤
17	V	V54NW02	PRE PACKING		S18051818	黨敬瑩	25678475 無錯誤
18	V	V54NW02	SN CHECK		V24001653	HÀ MINH HỢP	25678475 無錯誤
19	V	V54NW02	PACKING1	Check Acc	V24001653	HÀ MINH HỢP	25678475 無錯誤
20	V	V54NW02	PACKING WET_R		S12041706	何志傑	25678475 無錯誤
21	V	V54NW02	PACKING		S18051818	黨敬瑩	25678475 無錯誤
22	V	V54NW02	WEIGHT		S12041706	何志傑	25678475 無錯誤
23	V	V54NW02	PACKING WEIGHT		S18051818	黨敬瑩	25678475 無錯誤
24	V	VF15F01A	WE 90		S09605560	信帥	25678475 無錯誤

1						
STATION	GRP	INPUT	RW INPUT	Total Input	First Defect	First Yield Rate
Pre-test	TW4	0	1	1	0	100.00%
CHECK 下蓋	AI4	509	1	510	0	100.00%
Link電源	AI1	508	1	509	0	100.00%
INTERNAL INSPECTION	AD4	508	1	509	3	99.41%
列印機台Label	AI3	508	3	511	0	100.00%
CHECK 上蓋	AI2	508	3	511	0	100.00%
CHECK ML	AI5	507	2	509	0	100.00%
組裝外觀總檢	AD0	507	1	508	0	100.00%
Burn-In Input	AGI	506	3	509	0	100.00%
Burn-In output	TA0	509	3	512	80	84.38%
Final test	TS3	550	2	552	18	96.74%
Final check	TFC	551	1	552	3	99.46%
Software Download	TS0	551	2	553	3	99.46%
AOI check	KV0	562	0	562	0	100.00%
FQC	Q01	557	0	557	0	100.00%
	K07	536	0	536	0	100.00%
	T05	536	24	560	0	100.00%
Check Acc	PAK1	537	24	561	0	100.00%
OQC	OQC2	33	0	33	10	69.70%
	WEC	513	25	538	0	100.00%
	K10	512	128	640	0	100.00%
	WET	512	128	640	0	100.00%
	K02	528	168	696	0	100.00%
	W90	954	78	1032	0	100.00%
Total:		12002	599	12601	117	97.88%

Detailed Description of Work Results

CISCO Sky Eternal AOI Inspection

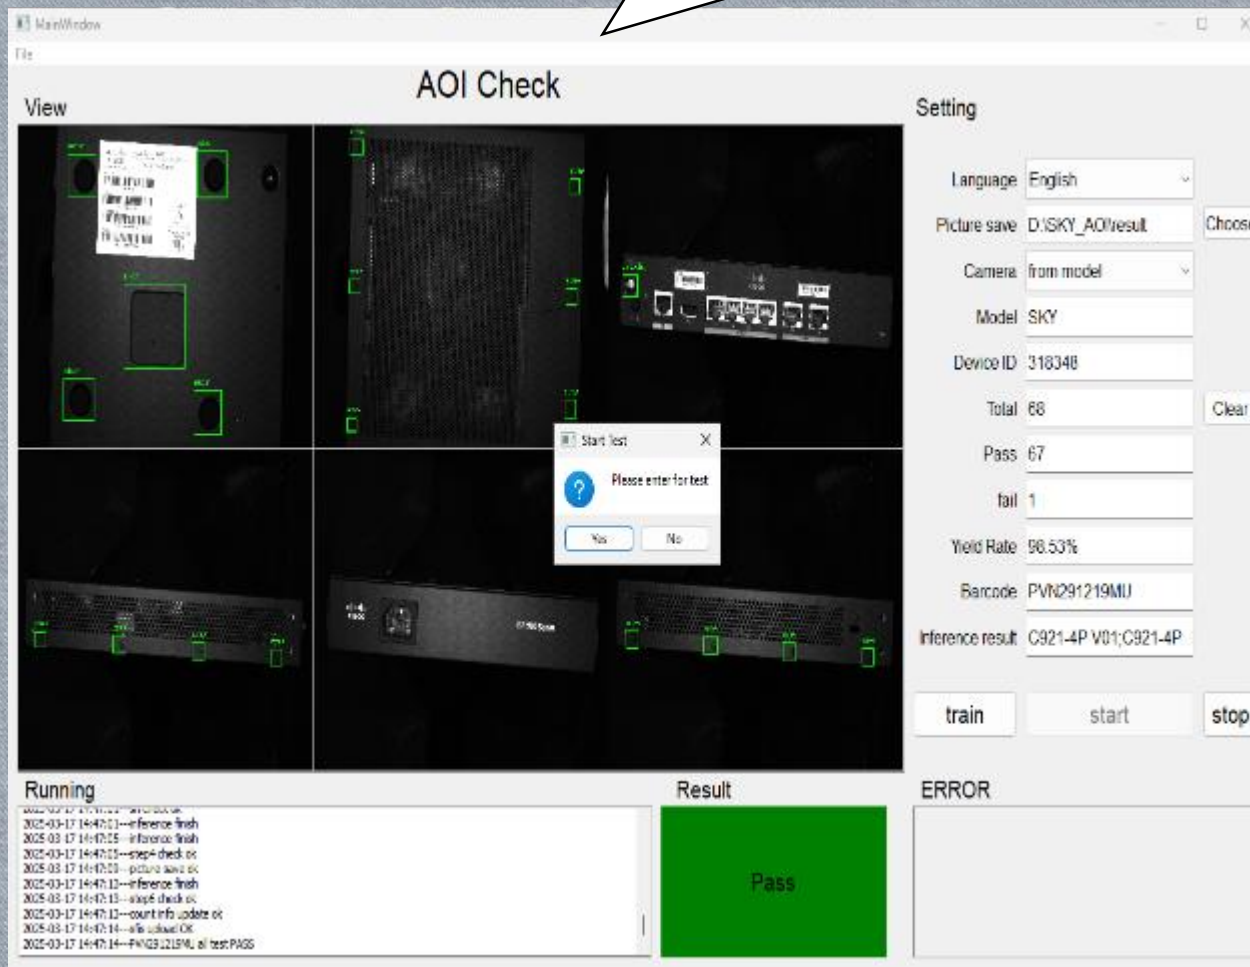

MO_ROUTE							
SEQ	SHOP	LINE	GRPNM	STEPNM	OP	OPNM	MO
1	V	V54NW04	ASSY INPUT		V24000675	NGUYỄN VĂN THẨM	25664364
2	V	V54NW04	ASSY KP INPUT1		V24004261	VŨ TRỌNG THỌ	25664364
3	V	V54NW04	ASSY KP INPUT2	AOI inspection	V24002776	NGUYỄN TUẤN ANH	25664364
4	V	V54NW04	OQC packing前離線驗		V23001023	LƯƠNG CAO TÙNG	25664364
5	V	V54NW04	WARM UP	2C Test	V24004464	PHẠM TUẤN KHANH	25664364
6	V	V54NW02	HI-PORT SEC TEST	Hi-pot	V24001614	LÊ XUÂN NAM	25664364
7	V	V54NW04	FUNCTION RETEST	Functional Test	V24003975	LÙ THỊ HOA	25664364
8	V	V54NW04	PACKING1	Check Acc	S18051818	黨敏瑩	25664364
9	V	V54NW04	DOWNLOAD TEST	SW Download	V24005007	HOÀNG QUỐC LUÂN	25664364
10	V	V54NW04	PRE PACKING	Packing_Input	S18051818	黨敏瑩	25664364
11	V	V54NW04	PRE PACKING FOR BOX	Check screw	V24000675	NGUYỄN VĂN THẨM	25664364
12	V	V54NW04	PACK Pre-VISUAL R	AOI take picture	V24002407	THAN NGOC LONG	25664364
13	V	V54NW04	OQC2	OQC	V23005026	NGUYỄN THỊ KHÁNH	25664364
14	V	V54NW04	PACK POST VISUAL2	Check SSN	V24000675	NGUYỄN VĂN THẨM	25664364
15	V	V54NW04	PACKING		S18051818	黨敏瑩	25664364
16	V	V54NW04	WEIGHT		S18051818	黨敏瑩	25664364
17	V	V54NW04	PACKING BOXING		S18051818	黨敏瑩	25664364
18	V	V54NW04	PACKING WEIGHT		S18051818	黨敏瑩	25664364
19	V	V54NW04	PACKING WEIGHT		S18051818	黨敏瑩	25664364

1						
STATION	GRP	INPUT	RW INPUT	Total Input	First Defect	First Yield Rate
	AI0	181	0	181	0	100.00%
	AI1	182	0	182	0	100.00%
AOI inspection	AI2	182	2	184	4	97.83%
	Q01	188	2	190	1	99.47%
2C Test	TWU	158	0	158	6	96.20%
Hi-pot	TH0	175	0	175	3	98.29%
Functional Test	TWC	183	0	183	3	98.36%
Check Acc	PAK1	186	12	198	0	100.00%
SW Download	TW0	210	4	214	13	93.93%
外觀總檢2	T7A	1	0	1	1	0.00%
Packing_Input	K07	218	3	221	0	100.00%
Check screw	K09	218	3	221	0	100.00%
AOI take picture	KV1	218	3	221	8	96.38%
FQC	OQC	37	0	37	2	94.59%
OQC	OQC2	206	0	206	0	100.00%
Check SSN	KV2	206	0	206	0	100.00%
	K10	186	0	186	0	100.00%
	WET	190	0	190	0	100.00%
	K01	190	0	190	0	100.00%
	K02	200	200	400	0	100.00%
Total:		3515	229	3744	41	93.75%

Detailed Description of Work Results


CISCO EZ1K/Lightsaber 8P Label Check AOI
(Running Offline)

MainWindow

File

AOI Check

View

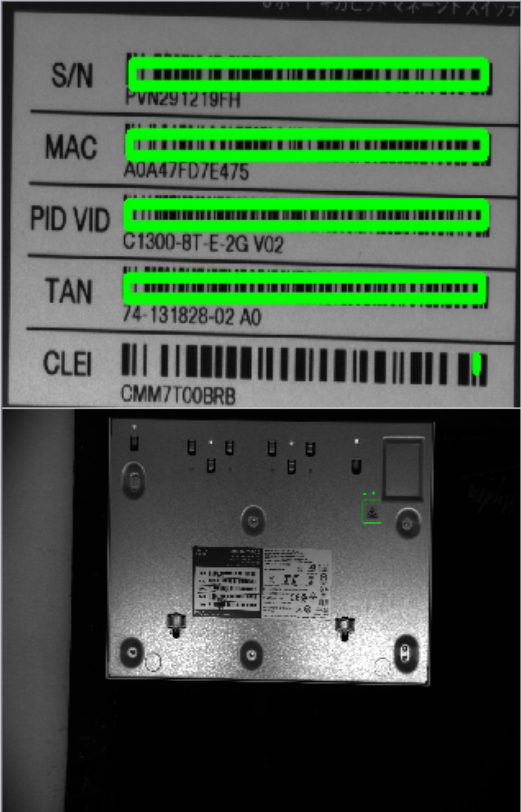

Setting

Language: English

Picture save: D:\newest_TP\result Choose

Camera: from model

Model: C1300-8T-E-2G

Device ID: 318342

Total: 1 Clear

Pass: 1

fail: 0

Yield Rate: 100.00%

Barcode: PVN291219FH

Inference result:

train start stop

Running

```
2025-03-17 14:52:30---label ocr finish!!!!
2025-03-17 14:52:30---barcode ocr3 bypass
2025-03-17 14:52:30---check ok,MfgDate(Date de Fab):20250317
2025-03-17 14:52:30---barcode ocr1 OK
2025-03-17 14:52:30---inference finish
2025-03-17 14:52:39---no nothing need to check
2025-03-17 14:52:39---no topdate need to check
2025-03-17 14:52:39---PVN291219FH all test PASS
2025-03-17 14:52:39---count info update ok
```

Result

Pass

ERROR

Detailed Description of Work Results


CISCO Somerset-Infra Eternal AOI
Inspection(Running Offline)

MainWindow

File

AOI Check

View

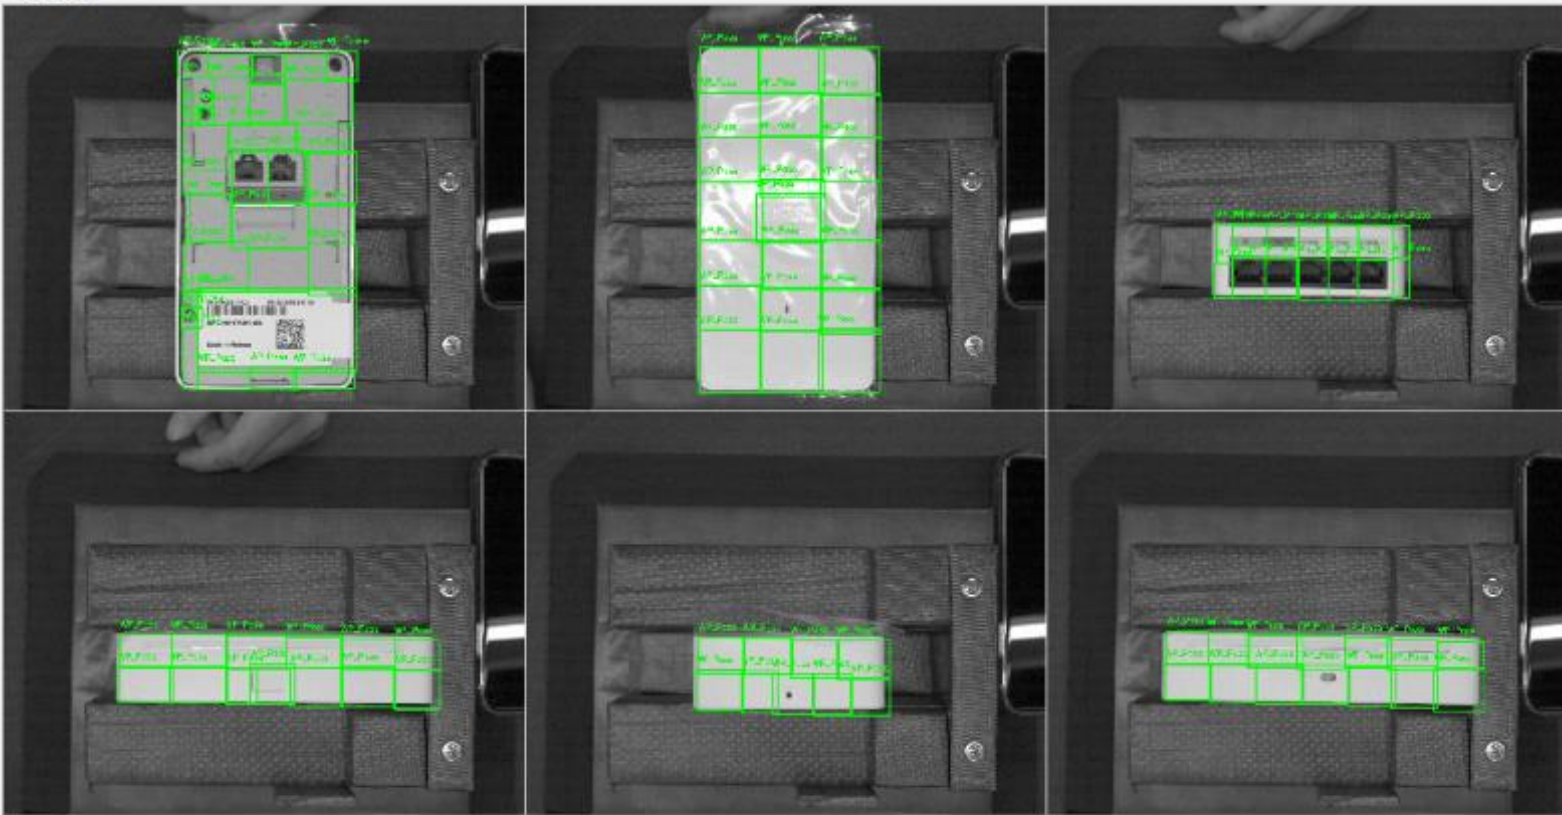

Setting

Language English

Picture save D:\Somerset_TP\result Choose

Camera from model

Model WP_check

Device ID 318342

Total 1 Clear

Pass 1

fail 0

Yield Rate 100.00%

Barcode PVN29111FQ3

Inference result

train start stop

Running

```
2025-03-17 15:02:17---step2 check ok  
2025-03-17 15:02:22---inference finish  
2025-03-17 15:02:33---inference finish  
2025-03-17 15:02:33---step4 check ok  
2025-03-17 15:02:39---inference finish  
2025-03-17 15:02:39---step5 check ok  
2025-03-17 15:02:43---inference finish  
2025-03-17 15:02:43---step6 check ok  
2025-03-17 15:02:43---count info update ok  
2025-03-17 15:02:43---PVN29111FQ3 all test PASS
```

Result

Pass

ERROR



Detailed Description of Work Results

1. What

- Description : “Product does not meet quality standards”
 - ✓ Products with missing or incorrect components.
 - ✓ Product is scratched, dented and deformed.
 - ✓ Product label does not comply with requirements.

2. Why

- Cause Analysis
 - ✓ Material is wrong, OP installed missing or wrong materials.
 - ✓ ME gives wrong instructions.
 - ✓ The product label is not correct compared to SOP.

3. Who

- AOI Team



Detailed Description of Work Results

4. Where

- Internal Inspection : Line 4A, 4B
- Outernal Inspection : Line 4A, 4B, 4C, 4J, 4K
- Label Checking : Line 4B

5. How

- Set up component identity software.
- Set up label data authentication software.

6. Data Result

- Decrease the defect rate.
- First Pass Yield (FPY) stable.
- Decrease the rework.
- Making OP work more comfortable.
- Preventing OP from wrong operation
- Improve product quality.



Future work and Self-Development Plans

Time	Work and Self-Development Plans	
2025 Q1~	Future work	1. Improve efficiency in processing speed
		2. Improve recognition for AOI Vision
		3. Explore new models and programs to optimize the program
		4. Optimize python code for program
	Self-development plans	1. Acquiring new skills, enhancing existing ones
		2. Improve communication skills in English and Chinese
		3. Expanding understanding in relevant areas : robot, plc, ...
		4. Enhance python and camera skills
		5. Improve adaptability to work problems

Recommendations for Departments

- The AOI team needs to be provided with laptops to facilitate their work.

A photograph of the entrance to a Pegatron factory in Vietnam. In the foreground, a white sign with black text reads 'PEGATRON ②' and 'CÔNG TY TNHH PEGATRON VIỆT NAM'. Below this, smaller text lists various products: 'SẢN PHẨM: LƯỚI LẠM, MÀN HÌNH LCD, MÁY INHATE, MÁY CẮT VÀI, BƠM HẤP HỖ, HỒ ÁM, HỒ THƯƠNG' and the address 'ĐIỂM THẠCH: 0000 000 0000'. The sign is set against a backdrop of a large industrial building with a modern, curved facade and a series of windows. The sky is overcast with grey clouds. A paved road leads towards the building, and a yellow barrier is visible on the right side of the road.

PEGATRON ②
CÔNG TY TNHH PEGATRON VIỆT NAM
SẢN PHẨM: LƯỚI LẠM, MÀN HÌNH LCD, MÁY INHATE, MÁY CẮT VÀI, BƠM HẤP HỖ, HỒ ÁM, HỒ THƯƠNG
ĐIỂM THẠCH: 0000 000 0000

Thank You
